

RAMP MODIFICATION

Quote Application Requirements For Department of Veteran Affairs (DVA) Clients

(THIS IS FOR MAJOR RAMPS WITH 1:10 OR 1:14 GRADIENT)

OPTION 1: INFORMATION REQUIRED IN ORDER FOR MAM TO DEVELOP A FORMAL QUOTE:

1. Funding Body
2. Client's Details – Name & Contact Number, Secondary Contact (if available)
3. Proposed Plan (With Detailed Measurements)
4. Existing Plan (With Detailed Measurements)
5. Existing photos of proposed area including a photo of entire area from a distance to look for potential issues with height restrictions and fall in land
6. General Scope of Works
7. Any specifications, e.g. painted rails, gate, mid rails, door magnet, non-slip paint, FRP Grating Walkway, any non-standard items, etc...



OPTION 2: To arrange a free onsite with MAM Draftsperson (Measure, Consult, Design & Quote), please send through some photos, a rough scope of work and fill out the Draftsperson Pre-Appointment Checklist, we will arrange a free onsite with our Draftsperson.

OPTION 3: Alternatively, you can also arrange your own Architect to provide us the above information.

Please see below an example of a ramp request with complete information (For Option-1)

Example application

Client name:
 Client contact number:
 Client address:
 Funding body:
 Occupational Therapist:
 OT contact number:
 OT email:

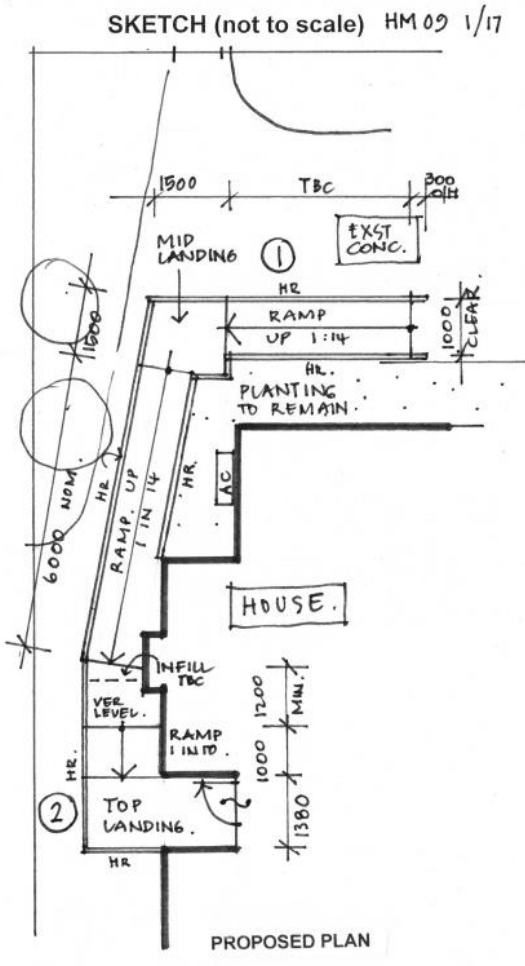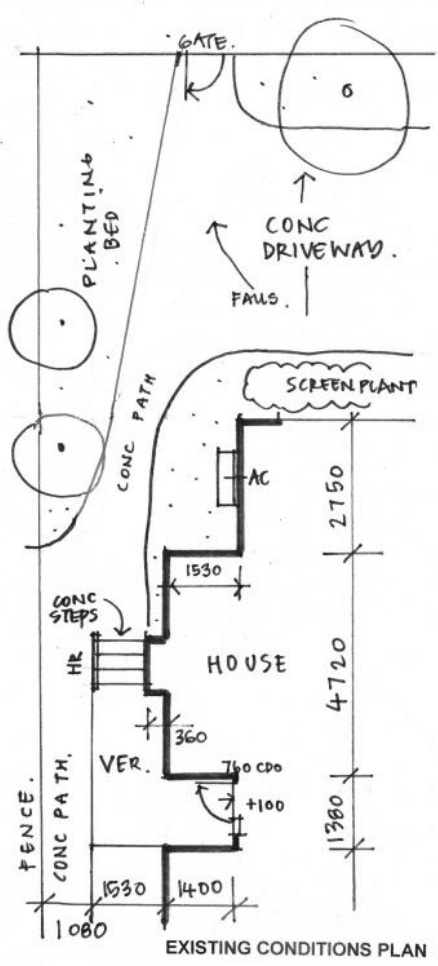

SCOPE OF WORKS – TIMBER RAMP
 BUILDER MUST VISIT SITE WHEN QUOTING AND CONFIRM ALL DIMENSIONS AND CONDITIONS PRIOR TO COMMENCEMENT OF ANY WORKS. NOTIFY O.T OR ARCHITECT OF ANY DISCREPANCIES OR CHANGES.

ALL WORK TO COMPLY WITH BCA AND A.S 1428.1 (WHERE APPLICABLE)

CLEAR ALL AREA AS REQUIRED FOR NEW RAMP.
 CUT BACK OR REMOVE SHRUBS AS REQ'D.

BUILD NEW TOP LANDING TO BE LEVEL WITH DOOR SILL.

BUILD NEW TIMBER RAMPS AS DRAWN. BUILD OVER EXST VERANDAH AND CONC DRIVE. INSTALL NEW 30-50 DIA. HANDRAILS AND KERBS TO RAMP.
 NOTE ANGLE RAMP AS REQ'D. CONFIRM ON SITE REFER TO STANDARD RAMP DETAIL.
 INSTALL DECKING REEDED SIDE DOWN AND ALUM PLATE AT THE COMMENCEMENT OF THE RAMPS AS PER DETAIL.

CONFIRM HAND RAIL HEIGHTS/MID RAIL WITH O.T AND CLIENT PRIOR TO INSTALLATION.

INSTALL A MAGNETIC DOOR STOP TO SCREEN DOOR.

CLEAR AWAY ALL RUBBISH ON COMPLETION.

HEIGHT (TBC)	
RAMP 1	710mm APPROX.
RAMP 2	100 mm APPROX
LENGTH	
RAMP 1	9940 mm APPROX.
RAMP 2	1000 mm APPROX.
MIN. GRADIENT	
RAMP 1	1 IN 14
RAMP 2	1 IN 10
MIN. WIDTH BETWEEN RAILS	1000 mm APPROX.
MIN. HANDRAIL CLEARANCE FROM ALL OBSTRUCTIONS	50 mm

PHOTOS

